

29th March 2021

Old War Office

Newsletter

Westminster Development Services Ltd

New Zealand House
80 Haymarket,
London
SW1Y 4TE

“Welcome to the 29th of March 2021 edition of the Old War Office Construction Newsletter, providing an update on the works taking place behind the hoarding at 57 Whitehall

Planned Work Activities

We continue to monitor the site and control the risk of C-19.

Progress continue on site and the revised guidance of the CLC are not affecting the measures put in place by Ardmore.

The external façade restoration / alterations to Whitehall Court are largely complete and the scaffolding to this elevation has been struck, the remaining section will be removed by end of May2021. Scaffold erection to Horse Guards Avenue completed. Stone cleaning and restoration work commence to this elevation in early March.

Installation of new Portland Stone continues at roof level.

The internal fit out of the new 125 Bedroom Hotel is proceeding to plan.

Fit Out of the 85 No New Residential Apartments is proceeding to plan with works commenced to circa 50 No apartments.

Work has commenced to fit out the new Hotel Spa.

Mechanical and Electrical Service installation works are ongoing within the new Plant Rooms at Basement levels.

We continue to install new Passenger and Goods Lifts across both the Residential and Hotel demises.”

“We have obtained permission from Westminster Council to remove our remaining Tower Crane over the weekend of 10th and 11th April 2021.

The works will entail the complete closure of Whitehall Place to all traffic over this weekend.

In order to limit traffic disruption, the works are planned to commence in the early hours of Saturday morning 10th April and continue until late Sunday evening 11th April 2021.

The dismantling works for Tower Crane 2 will follow the same sequence as the dismantling works undertaken for Tower Crane 1 in April last year. The works will be undertaken by Trident Tower Cranes.

The planned schedule is as follows -

Saturday 10th April 2021

1. Trident take possession of Whitehall Place at 2am
2. Diversion signs and fencing by Trident Traffic management placed from 2am to 3am
3. Mobile Crane and Slave Crane arrive at 2.30am and start rigging
4. Mobile Crane Rigged by 7.30am
5. Team briefing and inductions complete by 8am.
6. Dismantle works cease by 8pm

Sunday 11th April 2021

7. Dismantle commences at 7am
8. Dismantle completion by 6pm
9. Mobile Crane De-Rigged by 10pm
10. Site clear and tidy

Whitehall Place will be closed to traffic however the footpath will remain open as shown on the attached plan.

We apologise in advance of this inconvenience and will ensure that we limit any disruption caused.

Please contact us if you require any further information regarding these planned works."



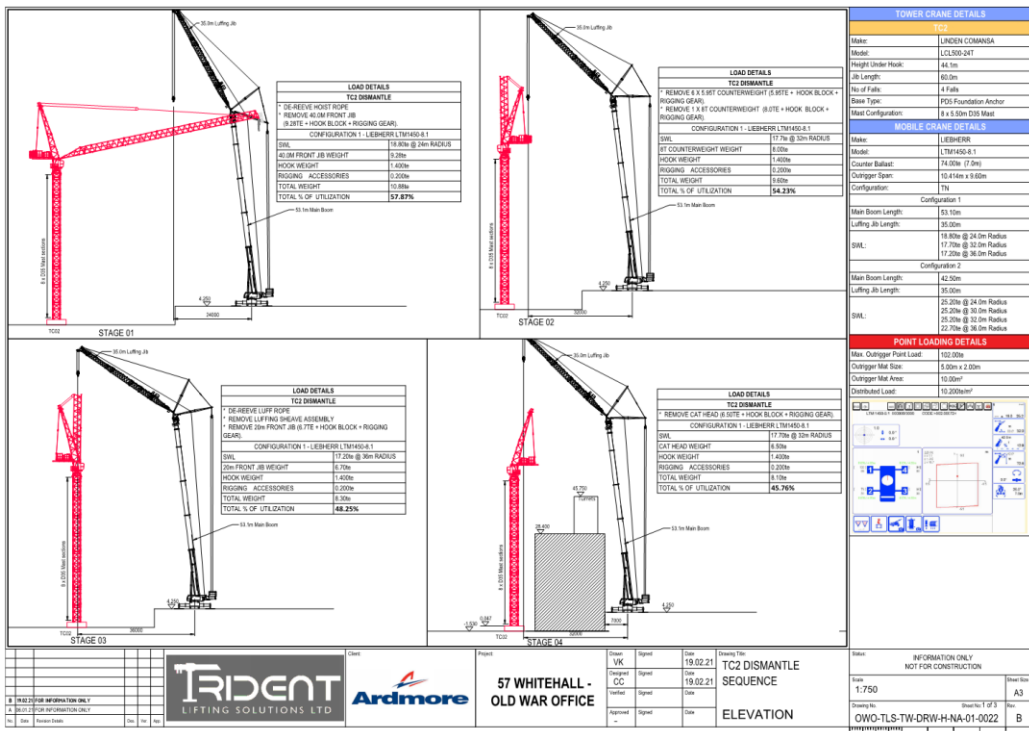


PHOTO GRAPHICAIC REPORT

BASEMENT 5.



Blockworks almost complete on the to the perimeter wall and started the internal walls, main plant installation continue.

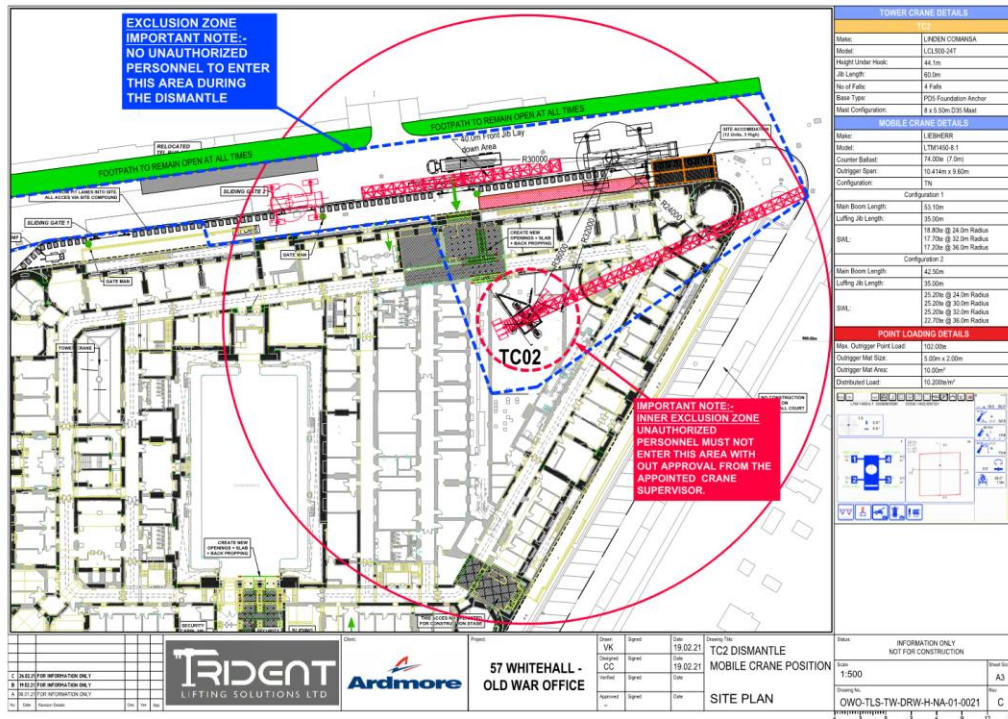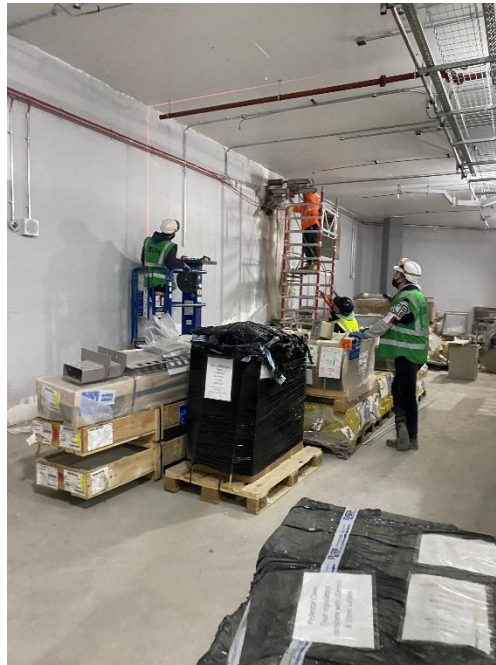

Basement 5 services installation and Car lift

BASEMENT 4 / 3



Main work vertical RC elements between B4&3 almost completed, builders work started on preparation form the first fix M&E.

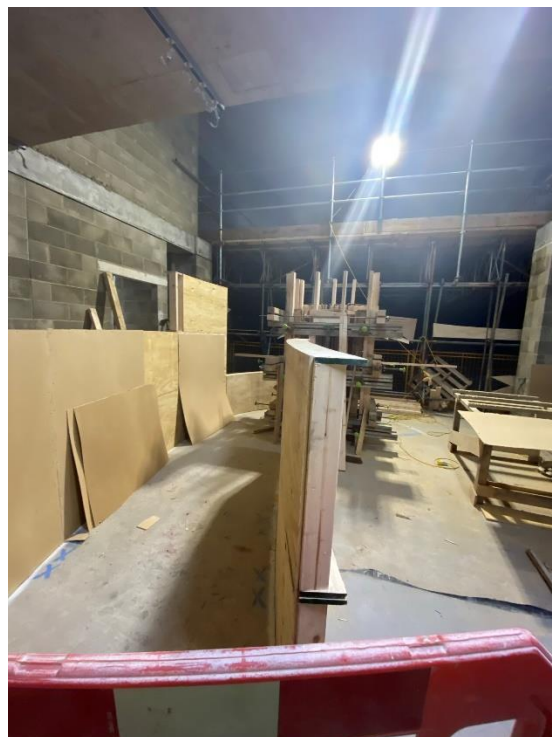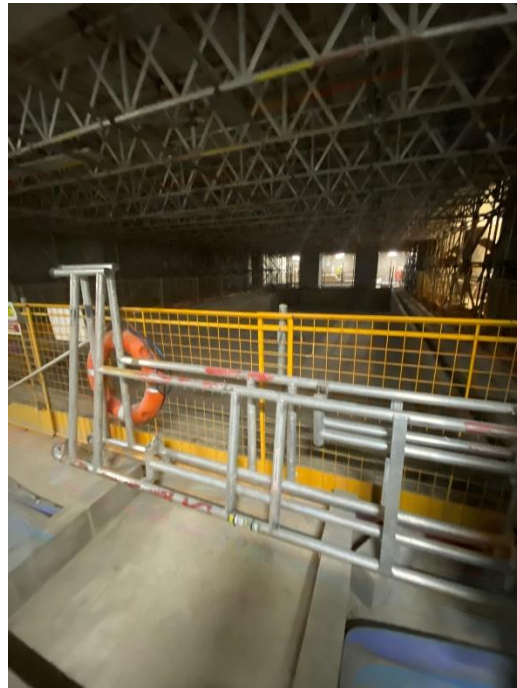

Basement 4 M&E installation plant room & Spa

BASEMENT 1 & 2.

Drainage works on going below the north Lightwell, Extension to the Grand Staircase to Basement, services tranches, and moat, plus the removal of the temporary piles and columns, the closure of the mole-holes.

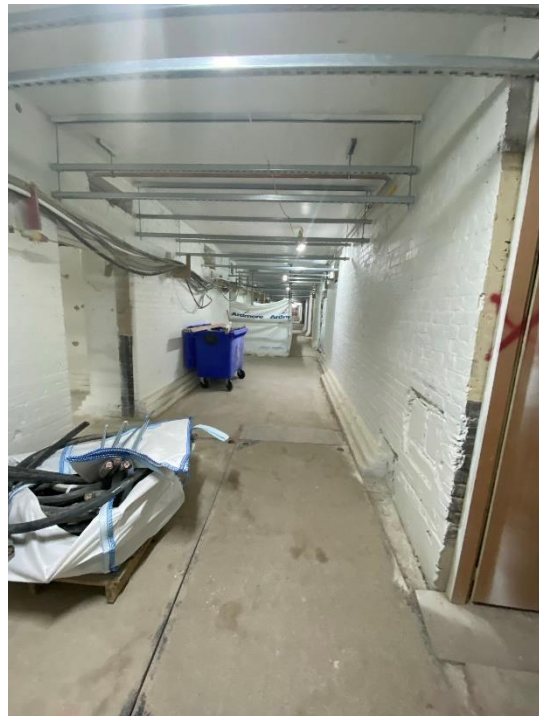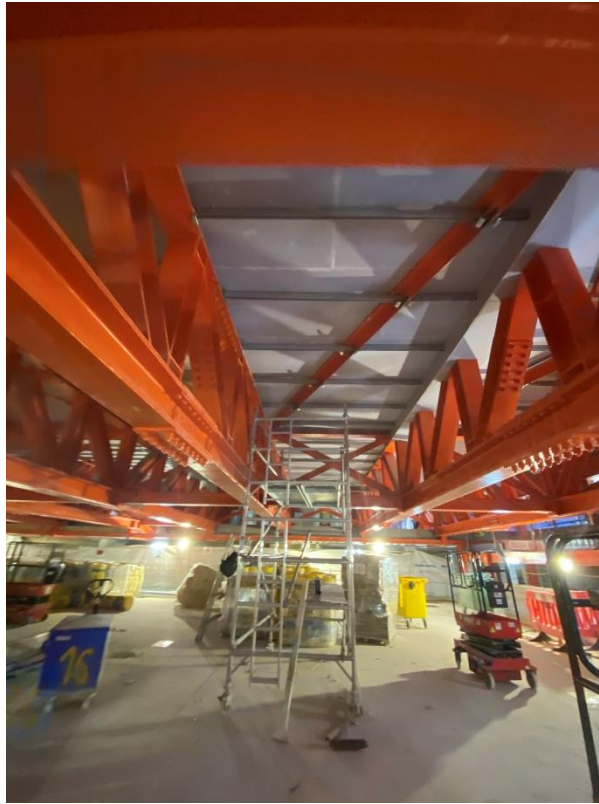



Basement 1 Back of House fitout

Ground Floor

Main logistic are, setting up new welfare, Resi Benchmark apartments, first fix resi fitout, waterproof & temporary protection works quadrangle, Start striping out FoH hotel new cladding Facade.



Triangular Courtyard

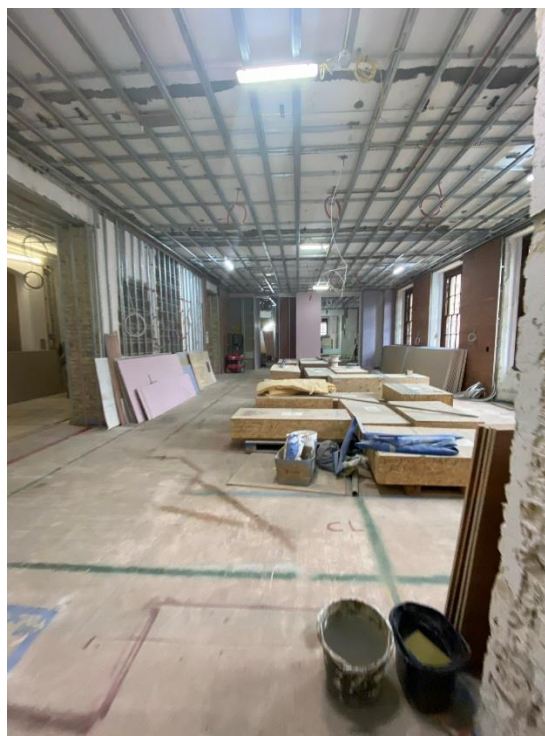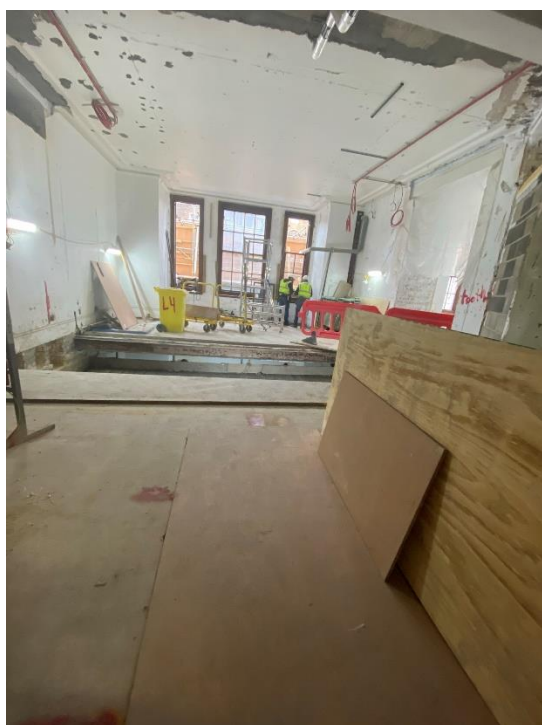


Ground floor FoH hotel.

1st to 4th Floor

Resi and Hotel Fitout works, external façade works with the Steel Framing System (SFS).




Level 2 Ceiling restauration

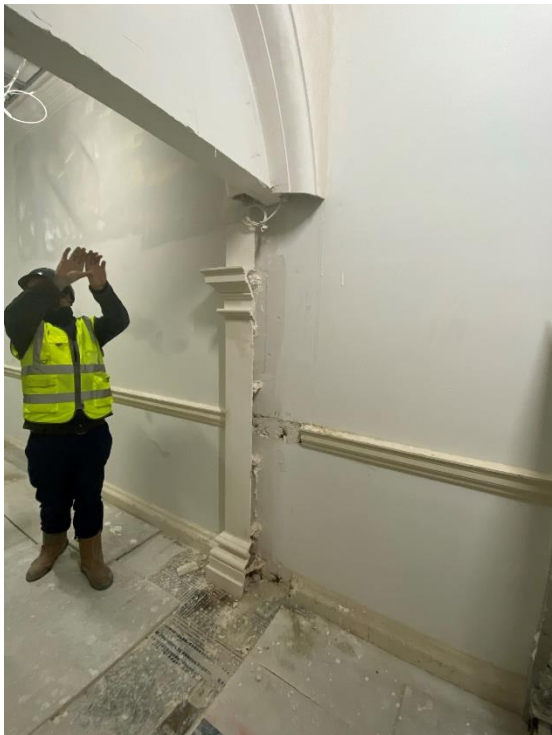

Level 3 Hotel Fitout

5th to Roof

Steel Framing System (SFS), Waterproofing, new and repair Stone wall and roof works, Start Drylining and first fix

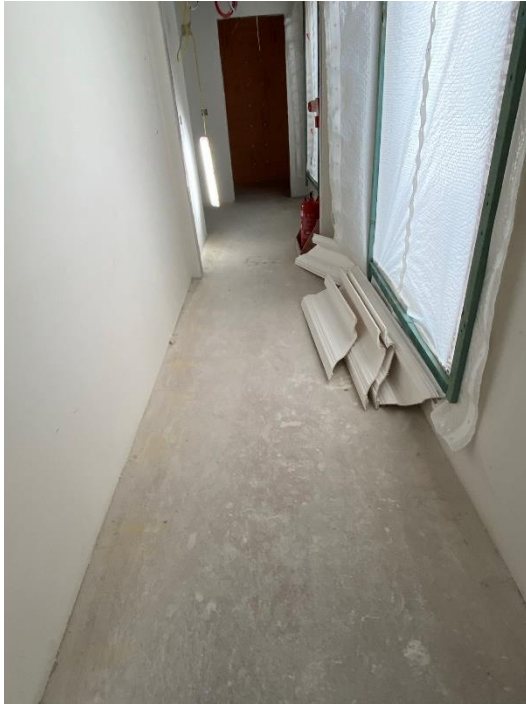

Level 5 Hotel Fitout
